


Pelham Road over Porcupine Brook Bi-Weekly Progress Report September 4, 2009

This report identifies work associated with the Pelham Road bridge project. Below is a summary of work that the contractor, DuBois Excavation completed in the last 2 weeks and anticipated work to be performed in the next 2 weeks.

Last 2 Weeks

- The cofferdam has been removed around the bridge and the stone has been placed at the inlet and outlet of the pipe.
- The approach slabs for the box culvert have been constructed.

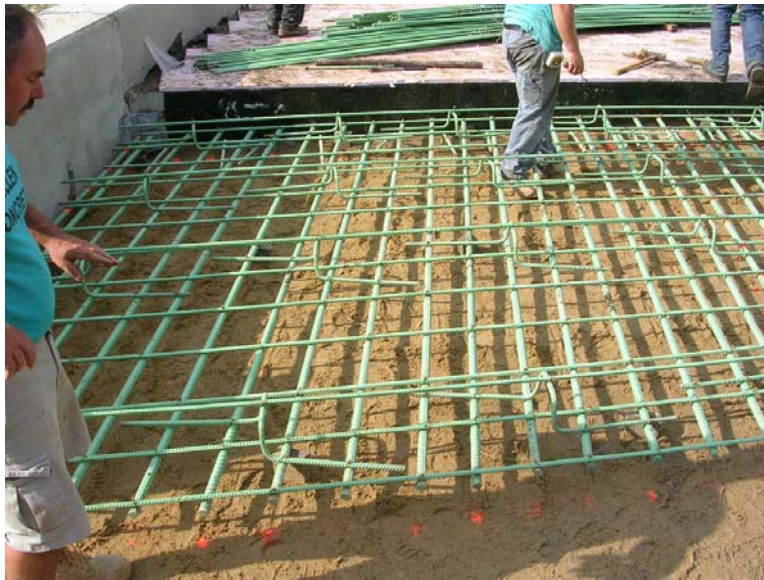

Gravels have been placed for the roadway.



Guard rail was erected on September 3rd. Paving is scheduled to be performed on Tuesday September 8. Following the placement of the pavement, there are just punch list items to complete.

Next 2 Weeks

- Paving and line striping
- Project cleanup and punch list items
- Possible road opening by 9/18/09
